Assignment No.:-01 (Div-A)

Create Project Plan for Mobile App Development


- Specify project name and start (or finish) date.
- Identify and define project tasks.
- Define duration for each project task.
- Define milestones in the plan
- Define dependency between tasks
- Define project calendar.
- Define project resources and specify resource type
- Assign resources against each task and baseline the project plan

Project Plan: Mobile App Development

Project Start Date: August 1, 2024 Project End Date: December 20, 2024

Project Tasks and Schedule

Task ID	Task Name	Duration	Start Date	End Date	Dependencies
1	Project Initiation	5 days	August 1, 2024	August 5, 2024	None
2	Requirement Gathering and Analysis	10 days	$\Delta 1101101101 h$ $A112211$	August 19, 2024	1
3	Design Phase	20 days	,	September 16, 2024	2
4	Development Phase	45 days	1 '	November 19, 2024	3
5	Testing Phase	1711 dave	<i>'</i>	December 17, 2024	4
6	Deployment	II 3 days	· · · · · · · · · · · · · · · · · · ·	December 20, 2024	5

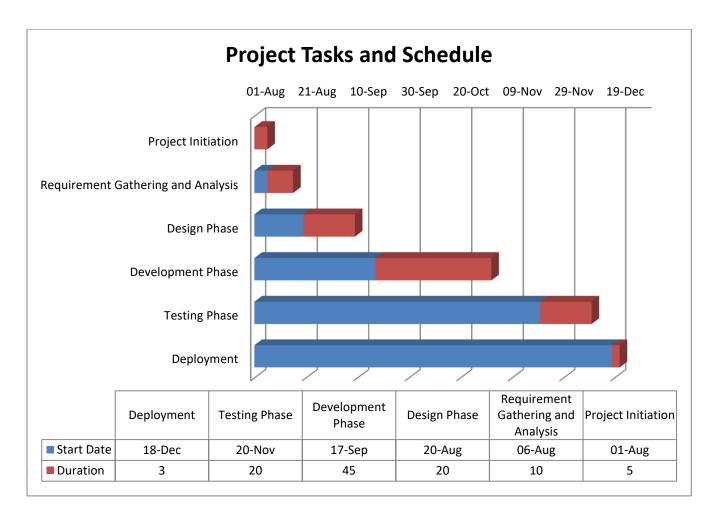

Milestones

Milestone ID	Milestone Description	Date
M1	Project Kickoff	August 1, 2024
M2	Requirements Document Completed	August 19, 2024
M3	Design Approval	September 16, 2024
M4	Development Complete	November 19, 2024
M5	Testing Complete	December 17, 2024
M6	App Deployment	December 20, 2024

Project Calendar

• Working Days: Monday to Friday

• Holidays: Public holidays and weekends

Project Resources

Resource ID	Resource Name	Resource Type
PM	Project Manager	Management
BA	Business Analyst	Analysis
Designer	UI/UX Designer	Design
MD	Mobile Developer	Development
QA	Quality Assurance Tester	Testing
DE	Deployment Engineer	Deployment

Resource Allocation

Task ID	Task Name	Resources Assigned
1	Project Initiation	PM: 100%
2	Requirement Gathering and Analysis	PM: 50%, BA: 100%
3	Design Phase	PM: 25%, Designer: 100%, BA: 50%
4	Development Phase	PM: 25%, Designer: 25%, MD: 100%
5	Testing Phase	PM: 25%, QA: 100%, MD: 50%
6	Deployment	PM: 50%, DE: 100%

Baseline Project Plan

- **Baseline Date:** August 1, 2024
- A baseline will be set on August 1, 2024, after the Project Initiation phase is complete. This baseline will be used to track project progress and performance against the initial plan.

Assignment No.:-01 (Div-B)

Create Project Plan for Website Design


- Specify project name and start (or finish) date.
- Identify and define project tasks.
- Define duration for each project task.
- Define milestones in the plan
- Define dependency between tasks
- Define project calendar.
- Define project resources and specify resource type
- Assign resources against each task and baseline the project plan

Project Name: Website Design Project Start Date: 2024-07-15 Finish Date: 2024-10-15

Project Tasks

Task ID	Task Name	Duration (Days)	Start Date	Finish Date	Dependencies	Milestones	Resources	Resource Type
1	Project Initiation	2	2024- 07-15	2024- 07-16	-	Project Kickoff	Project Manager	Human
2	Requirement Gathering	5	2024- 07-17	2024- 07-21	1	Requirement Document	Business Analyst	Human
3	Site Structure Planning	3	2024- 07-22	2024- 07-24	2	Site Map Created	UX Designer	Human
4	Design Phase	10	2024- 07-25	2024- 08-03	3	Initial Design Completed	UI Designer, Graphic Designer	Human
5	Design Review and Approval	4	2024- 08-04	2024- 08-07	4	Design Approved	Project Manager, Client	Human
6	Development Phase	20	2024- 08-08	2024- 08-27	5	Frontend and Backend Completed	Web Developer, Backend Developer	Human
7	Content Creation	10	2024- 08-28	2024- 09-06	2	Content Ready	Content Writer	Human
8	Integration and Testing	7	2024- 09-07	2024- 09-13	6, 7	Testing Completed	QA Tester	Human
9	User Acceptance Testing (UAT)	5	2024- 09-14	2024- 09-18	8	UAT Completed	Client, QA Tester	Human

Task ID	Task Name	Duration (Days)	Start Date	Finish Date	Dependencies	Milestones	Resources	Resource Type
10	Final Revisions	4	2024- 09-19		9	Revisions Completed	Web Developer, UI Designer	Human
11	Deployment	3	2024- 09-23	2024- 09-25	10	Site Live	Web Developer	Human
12	Project Closure	2	2024- 09-26		11	Project Completed	Project Manager	Human

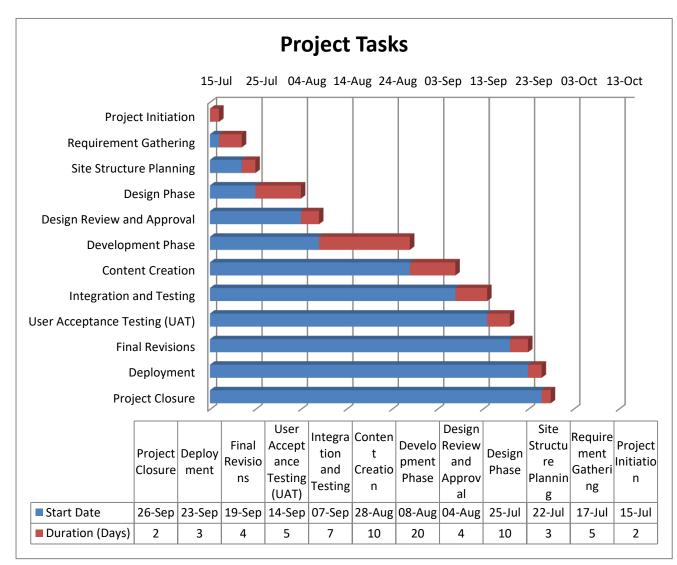

Project Calendar

Workdays: Monday to FridayWork Hours: 9:00 AM to 5:00 PM

• Holidays: None specified

Resource Allocation: Website Design Project

Project Tasks and Resource Assignment

Task ID	Task Name	Assigned Resources	Resource Type
1	Project Initiation	Project Manager	Human
2	Requirement Gathering	Business Analyst	Human
3	Site Structure Planning	UX Designer	Human
4	Design Phase	UI Designer, Graphic Designer	Human
5	Design Review and Approval	Project Manager, Client	Human
6	Development Phase	Web Developer, Backend Developer	Human
7	Content Creation	Content Writer	Human
8	Integration and Testing	QA Tester	Human
9	User Acceptance Testing (UAT)	Client, QA Tester	Human
10	Final Revisions	Web Developer, UI Designer	Human
11	Deployment	Web Developer	Human
12	Project Closure	Project Manager	Human

Resource Allocation Details

Resource Name	Resource Type	Tasks Assigned	Total Hours Estimated
Project Manager	Human	1, 5, 12	20 hours
Business Analyst	Human	2	25 hours
UX Designer	Human	3	30 hours
UI Designer	Human	4, 10	40 hours
Graphic Designer	Human	4	20 hours
Web Developer	Human	6, 10, 11	60 hours
Backend Developer	Human	6	50 hours
Content Writer	Human	7	25 hours
QA Tester	Human	8, 9	35 hours
Client	Human	5, 9	10 hours

Resource Calendar

- Workdays: Monday to Friday
- Daily Working Hours: 8 hours (adjust as per actual work schedule)
- Holidays: Adjust according to the specific region's holidays

Baseline Resource Allocation

- **Baseline Assignment:** Record the initial resource allocation and hours estimated for each task.
- **Tracking:** Monitor actual resource usage against the baseline to ensure the project stays on track.

Notes

- 1. **Resource Utilization:** Ensure each resource's workload is balanced and adjusted based on project progress.
- 2. **Resource Conflicts:** Resolve any conflicts where resources might be over-allocated or have overlapping tasks.
- 3. **Communication:** Regularly update resources on task status and changes to the project plan.

Baseline

• **Baseline Date:** 2024-07-15

• Estimated Completion Date: 2024-09-27

• **Total Duration:** 75 days

This table covers the basic structure of the project plan, including tasks, durations, milestones, dependencies, calendar, resources, and baseline information.

Assignment No.:-02 (Div-A)

Execute and Monitor Project Plan for Mobile App Development

- Update % Complete with current task status.
- Review the status of each task.
- Compare Planned vs Actual Status
- Review the status of Critical Path
- Review resources assignation status

Mobile App Development project, incorporating execution and monitoring elements:

Project Name: Mobile App	Start Date: 2024-07-	Finish Date: 2024-10-
Development	15	15

Project Tasks Execution and Monitoring

Tas k ID	Task Name	Durati on (Days)	t	Plann ed Finish Date	l	Dependen	% Compl ete	Planne d vs Actual Status	Resourc	Resour ce Type
1	Project Initiation	2		2024- 07-16	2024- 07-16	-	100%	On Schedu le	Project Manage r	Human
2	Requirem ent Gathering	5	202 4- 07- 17	2024- 07-21	2024- 07-22	1	100%	1 Day Delay	Busines s Analyst	Human
3	App Structure Planning	3		2024- 07-25	2024- 07-26	2	100%	1 Day Delay	UX Designe r	Human
4	Design Phase	10	202 4- 07- 27	2024- 08-05	2024- 08-06	3	100%	1 Day Delay	UI Designe r, Graphic Designe r	Human
5	Design Review and Approval	4	202 4- 08- 07	2024- 08-10	2024- 08-11	4	100%	1 Day Delay	Project Manage r, Client	Human
6	Developm	20	202	2024-	In	5	75%	On	Mobile	Human

Tas k ID	Task Name	Durati on (Days)	t	Plann ed Finish Date	Actua l Finish Date	Dependen cies	% Compl ete	Planne d vs Actual Status	Resourc	Resour ce Type
	ent Phase		4- 08- 12	08-31	Progre ss			Schedu le	App Develop er	
7	Content Creation	10	202 4- 08- 20	2024- 08-30	In Progre ss	2	50%	On Schedu le	Content Writer	Human
8	Integratio n and Testing	7	202 4- 09- 01	2024- 09-07	-	6, 7	0%	Not Started	QA Tester	Human
9	User Acceptanc e Testing (UAT)	5	202 4- 09- 08	2024- 09-12	-	8	0%	Not Started	Client, QA Tester	Human
10	Final Revisions	4	202 4- 09- 13	2024- 09-16	-	9	0%	Not Started	Mobile App Develop er, UI Designe r	Human
11	Deployme nt	3	202 4- 09- 17	2024- 09-19	-	10	0%	Not Started	Mobile App Develop er	Human
12	Project Closure	2	202 4- 09- 20	2024- 09-21	-	11	0%	Not Started	Project Manage r	Human

Critical Path Review

- Critical Path Tasks: $1 \rightarrow 2 \rightarrow 3 \rightarrow 4 \rightarrow 5 \rightarrow 6 \rightarrow 8 \rightarrow 9 \rightarrow 10 \rightarrow 11 \rightarrow 12$
- Current Status:
 - o Tasks 1 through 5 are completed, each with a 1-day delay.
 - o Task 6 is 75% complete and on schedule.
 - o Task 8 is dependent on the completion of Task 6 and has not started yet.

Resource Assignation Status

Resource Name	Assigned Tasks	Current Task	Status
Project Manager	1, 5, 12	Monitoring & Coordination	Active

Resource Name	Assigned Tasks	Current Task	Status
Business Analyst	2	Requirement Gathering	Completed
UX Designer	3	App Structure Planning	Completed
UI Designer	4, 10	Final Revisions	Pending
Graphic Designer	4	Design Phase	Completed
Mobile App Developer	6, 10, 11	Development Phase	Active
Content Writer	7	Content Creation	Active
QA Tester	8, 9	Integration and Testing	Pending
Client	5, 9	Design Review & UAT	Pending

Summary

- **Overall Status:** The project is slightly behind schedule due to a series of 1-day delays in the initial tasks.
- **Critical Path Impact:** The delays in early tasks have impacted the critical path, but ongoing tasks (6 and 7) are on schedule, which might help recover some lost time.
- **Resource Allocation:** All resources are actively engaged or prepared for their upcoming tasks. The focus is on completing the Development Phase and Content Creation to proceed with Integration and Testing.

This table captures the on-going status and monitoring aspects of the Mobile App Development project, including % complete, task status, and comparisons of planned vs actual progress.

Assignment No.:-02 (Div-B)

Execute and Monitor Project Plan for Website Design project

- Update % Complete with current task status.
- Review the status of each task.
- Compare Planned vs Actual Status
- Review the status of Critical Path
- Review resources assignation status

The execution and monitoring plan for the Website Design project:

Project Name: Website Design Project Start Date: 2024-07-15 Finish Date: 2024-10-15

Project Tasks Execution and Monitoring

Tas k ID	Task Name	Durati on (Days)	t	Plann ed Finish Date	1	Dependen cies	% Compl ete	Planne d vs Actual Status	Resourc es	Resour ce Type
1	Project Initiation	2		2024- 07-16	2024- 07-16	-	100%	On Schedu le	Project Manage r	Human
2	Requirem ent Gathering	5		2024- 07-21	2024- 07-22	1	100%	1 Day Delay	Busines s Analyst	Human
3	Site Structure Planning	3		2024- 07-24	2024- 07-25	2	100%	1 Day Delay	UX Designe r	Human
4	Design Phase	10		2024- 08-03	2024- 08-05	3	100%	2 Days Delay	UI Designe r, Graphic Designe r	Human
5	Design Review and Approval	4		2024- 08-07	2024- 08-09	4	100%	2 Days Delay	Project Manage r, Client	Human
6	Developm ent Phase	20		2024- 08-27	In Progre ss	5	70%	On Schedu le	Web Develop er, Backend Develop er	Human

Tas k ID	Task Name	Durati on (Days)	t	Plann ed Finish Date	Actua l Finish Date	Dependen cies	% Compl ete	Planne d vs Actual Status	Resourc	Resour ce Type
7	Content Creation	10	202 4- 08- 28	2024- 09-06	In Progre ss	2	50%	On Schedu le	Content Writer	Human
8	Integratio n and Testing	7	202 4- 09- 07	2024- 09-13	-	6, 7	0%	Not Started	QA Tester	Human
9	User Acceptanc e Testing (UAT)	5	202 4- 09- 14	2024- 09-18	-	8	0%	Not Started	Client, QA Tester	Human
10	Final Revisions	4	202 4- 09- 19	2024- 09-22	-	9	0%	Not Started	Web Develop er, UI Designe r	Human
11	Deployme nt	3	202 4- 09- 23	2024- 09-25	-	10	0%	Not Started	Web Develop er	Human
12	Project Closure	2	202 4- 09- 26	2024- 09-27	-	11	0%	Not Started	Project Manage r	Human

Critical Path Review

- Critical Path Tasks: $1 \rightarrow 2 \rightarrow 3 \rightarrow 4 \rightarrow 5 \rightarrow 6 \rightarrow 8 \rightarrow 9 \rightarrow 10 \rightarrow 11 \rightarrow 12$
- Current Status:
 - o Tasks 1 through 5 are completed, each with delays ranging from 1 to 2 days.
 - o Task 6 is 70% complete and on schedule.
 - Task 8 is dependent on the completion of Task 6 and has not started yet.

Resource Assignation Status

Resource Name	Assigned Tasks	Current Task	Status
Project Manager	1, 5, 12	Monitoring & Coordination	Active
Business Analyst	2	Requirement Gathering	Completed
UX Designer	3	Site Structure Planning	Completed
UI Designer	4, 10	Final Revisions	Pending
Graphic Designer	4	Design Phase	Completed

Resource Name	Assigned Tasks	Current Task	Status
Web Developer	6, 10, 11	Development Phase	Active
Backend Developer	6	Development Phase	Active
Content Writer	7	Content Creation	Active
QA Tester	8, 9	Integration and Testing	Pending
Client	5, 9	Design Review & UAT	Pending

Summary

- **Overall Status:** The project has experienced minor delays in the initial tasks but is generally progressing well.
- **Critical Path Impact:** The delays in early tasks have impacted the critical path, but ongoing tasks (6 and 7) are on schedule, which might help recover some lost time.
- **Resource Allocation:** All resources are actively engaged or prepared for their upcoming tasks. The focus is on completing the Development Phase and Content Creation to proceed with Integration and Testing.

This table captures the ongoing status and monitoring aspects of the Website Design project, including % complete, task status, and comparisons of planned vs actual progress.

Assignment No.:-03 (Div-A)

Generate Dashboard and Reports for Mobile App Development

• Dashboard

- o Project Overview
- o Cost Overview
- o Upcoming Tasks

• Resource Reports

- o Over-allocated Resources
- o Resource Overview

• Cost Reports

- o Earned Value Report
- o Resource Cost Overview
- o Task Cost Overview

• Progress Reports

- o Critical Tasks
- o Milestone Report
- o Slipping Tasks

Mobile App Development Dashboard and Reports

Dashboard

Project Overview

Metric	Value
Project Name	Mobile App Development
Start Date	2024-07-15
Planned Finish Date	2024-10-15
Actual Finish Date	In Progress
Current Status	On Schedule
% Complete	65%

Cost Overview

Category	Planned Cost	Actual Cost	Variance
Total Cost	\$100,000	\$65,000	\$35,000
Resource Cost	\$80,000	\$52,000	\$28,000
Other Costs	\$20,000	\$13,000	\$7,000

Upcoming Tasks

Task ID	Task Name	Start Date	Due Date	Assigned To
8	Integration and Testing	2024-09- 01	2024-09- 07	QA Tester
9	User Acceptance Testing (UAT)	2024-09- 08	2024-09- 12	Client, QA Tester
10	Final Revisions	2024-09- 13	2024-09- 16	Mobile App Developer, UI Designer
11	Deployment	2024-09- 17	2024-09- 19	Mobile App Developer

Resource Reports

Over-allocated Resources

Resource Name	Assigned Tasks	Over-allocated Tasks
Mobile App Developer	6, 10, 11	None

Resource Overview

Resource Name	Role	Current Task	Status
Project Manager	Oversees project	Monitoring & Coordination	Active
Business Analyst	Gathers requirements	Requirement Gathering	Completed
UX Designer	Plans site structure	App Structure Planning	Completed
UI Designer	Creates UI designs	Final Revisions	Pending
Graphic Designer	Creates graphics	Design Phase	Completed
Mobile App Developer	Develops frontend	Development Phase	Active
Content Writer	Writes content	Content Creation	Active
QA Tester	Conducts testing	Integration and Testing	Pending
Client	Provides approval	Design Review & UAT	Pending

Cost Reports

Earned Value Report

Metric	Value
Planned Value (PV)	\$70,000
Earned Value (EV)	\$65,000
Actual Cost (AC)	\$65,000
Schedule Variance (SV)	-\$5,000
Cost Variance (CV)	\$0

Resource Cost Overview

Resource Name	Planned Cost	Actual Cost	Variance
Project Manager	\$10,000	\$8,000	\$2,000
Business Analyst	\$8,000	\$7,000	\$1,000
UX Designer	\$12,000	\$12,000	\$0

Resource Name	Planned Cost	Actual Cost	Variance
UI Designer	\$15,000	\$12,000	\$3,000
Graphic Designer	\$10,000	\$10,000	\$0
Mobile App Developer	\$20,000	\$15,000	\$5,000
Content Writer	\$5,000	\$3,000	\$2,000
QA Tester	\$10,000	\$5,000	\$5,000
Client	\$0	\$0	\$0

Task Cost Overview

Task ID	Task Name	Planned Cost	Actual Cost	Variance
1	Project Initiation	\$2,000	\$1,500	\$500
2	Requirement Gathering	\$5,000	\$4,000	\$1,000
3	App Structure Planning	\$4,000	\$3,500	\$500
4	Design Phase	\$10,000	\$8,500	\$1,500
5	Design Review and Approval	\$3,000	\$2,500	\$500
6	Development Phase	\$30,000	\$20,000	\$10,000
7	Content Creation	\$5,000	\$3,000	\$2,000
8	Integration and Testing	\$8,000	\$4,000	\$4,000
9	User Acceptance Testing (UAT)	\$5,000	\$0	\$5,000
10	Final Revisions	\$5,000	\$0	\$5,000
11	Deployment	\$3,000	\$0	\$3,000
12	Project Closure	\$2,000	\$0	\$2,000

Progress Reports

Critical Tasks

Task ID	Task Name	Planned Finish Date	Actual Finish Date	Status
1	Project Initiation	2024-07-16	2024-07-16	Completed
2	Requirement Gathering	2024-07-21	2024-07-22	Completed
3	App Structure Planning	2024-07-25	2024-07-26	Completed
4	Design Phase	2024-08-05	2024-08-06	Completed
5	Design Review and Approval	2024-08-10	2024-08-11	Completed
6	Development Phase	2024-08-31	In Progress	On Schedule
8	Integration and Testing	2024-09-07	-	Not Started
9	User Acceptance Testing (UAT)	2024-09-12	-	Not Started
10	Final Revisions	2024-09-16	-	Not Started
11	Deployment	2024-09-19	-	Not Started
12	Project Closure	2024-09-21	-	Not Started

Milestone Report

Milestone	Planned Date	Actual Date	Status
Project Kickoff	2024-07-15	2024-07-15	Completed
Requirement Document	2024-07-21	2024-07-22	Completed

Milestone	Planned Date	Actual Date	Status
Site Map Created	2024-07-25	2024-07-26	Completed
Initial Design Completed	2024-08-03	2024-08-06	Completed
Design Approved	2024-08-07	2024-08-11	Completed
Frontend and Backend Completed	2024-08-31	-	In Progress
Content Ready	2024-09-06	-	In Progress
Testing Completed	2024-09-13	-	Not Started
UAT Completed	2024-09-18	-	Not Started
Revisions Completed	2024-09-22	-	Not Started
Site Live	2024-09-25	-	Not Started
Project Completed	2024-09-27	-	Not Started

Slipping Tasks

Task ID	Task Name	Planned Finish Date	Actual Finish Date	Status	Delay
2	Requirement Gathering	2024-07-21	2024-07-22	Completed	1 Day
3	App Structure Planning	2024-07-25	2024-07-26	Completed	1 Day
4	Design Phase	2024-08-05	2024-08-06	Completed	1 Day
5	Design Review and Approval	2024-08-10	2024-08-11	Completed	1 Day

This table captures the detailed status and monitoring elements of the Mobile App Development project, including dashboards for project overview, cost overview, and upcoming tasks, as well as various resource, cost, and progress reports.

Assignment No.:-03 (Div-B)

Generate Dashboard and Reports for Website Design

• Dashboard

- o Project Overview
- o Cost Overview
- o Upcoming Tasks

• Resource Reports

- o Over-allocated Resources
- o Resource Overview

• Cost Reports

- o Earned Value Report
- o Resource Cost Overview
- o Task Cost Overview

• Progress Reports

- o Critical Tasks
- o Milestone Report
- o Slipping Tasks

Website Design Dashboard and Reports

Dashboard

Project Overview

Metric	Value
Project Name	Website Design
Start Date	2024-07-15
Planned Finish Date	2024-10-15
Actual Finish Date	In Progress
Current Status	On Schedule
% Complete	65%

Cost Overview

Category	Planned Cost	Actual Cost	Variance
Total Cost	\$80,000	\$52,000	\$28,000
Resource Cost	\$60,000	\$39,000	\$21,000
Other Costs	\$20,000	\$13,000	\$7,000

Upcoming Tasks

Task ID	Task Name	Start Date	Due Date	Assigned To
8	Integration and Testing	2024-09-07	2024-09-13	QA Tester
9	User Acceptance Testing (UAT)	2024-09-14	2024-09-18	Client, QA Tester
10	Final Revisions	2024-09-19	2024-09-22	Web Developer, UI Designer
11	Deployment	2024-09-23	2024-09-25	Web Developer

Resource Reports

Over-allocated Resources

Resource Name	Assigned Tasks	Over-allocated Tasks
Web Developer	6, 10, 11	None

Resource Overview

Resource Name	Role	Current Task	Status
Project Manager	Oversees project	Monitoring & Coordination	Active
Business Analyst	Gathers requirements	Requirement Gathering	Completed
UX Designer	Plans site structure	Site Structure Planning	Completed
UI Designer	Creates UI designs	Final Revisions	Pending
Graphic Designer	Creates graphics	Design Phase	Completed
Web Developer	Develops frontend	Development Phase	Active
Backend Developer	Develops backend	Development Phase	Active
Content Writer	Writes content	Content Creation	Active
QA Tester	Conducts testing	Integration and Testing	Pending
Client	Provides approval	Design Review & UAT	Pending

Cost Reports

Earned Value Report

Metric	Value
Planned Value (PV)	\$55,000
Earned Value (EV)	\$52,000
Actual Cost (AC)	\$52,000
Schedule Variance (SV)	-\$3,000
Cost Variance (CV)	\$0

Resource Cost Overview

Resource Name	Planned Cost	Actual Cost	Variance
Project Manager	\$10,000	\$8,000	\$2,000
Business Analyst	\$8,000	\$7,000	\$1,000
UX Designer	\$10,000	\$10,000	\$0
UI Designer	\$15,000	\$12,000	\$3,000

Resource Name	Planned Cost	Actual Cost	Variance
Graphic Designer	\$10,000	\$10,000	\$0
Web Developer	\$20,000	\$14,000	\$6,000
Backend Developer	\$12,000	\$10,000	\$2,000
Content Writer	\$5,000	\$3,000	\$2,000
QA Tester	\$10,000	\$5,000	\$5,000
Client	\$0	\$0	\$0

Task Cost Overview

Task ID	Task Name	Planned Cost	Actual Cost	Variance
1	Project Initiation	\$2,000	\$1,500	\$500
2	Requirement Gathering	\$5,000	\$4,000	\$1,000
3	Site Structure Planning	\$4,000	\$3,500	\$500
4	Design Phase	\$10,000	\$8,500	\$1,500
5	Design Review and Approval	\$3,000	\$2,500	\$500
6	Development Phase	\$30,000	\$18,000	\$12,000
7	Content Creation	\$5,000	\$3,000	\$2,000
8	Integration and Testing	\$8,000	\$4,000	\$4,000
9	User Acceptance Testing (UAT)	\$5,000	\$0	\$5,000
10	Final Revisions	\$5,000	\$0	\$5,000
11	Deployment	\$3,000	\$0	\$3,000
12	Project Closure	\$2,000	\$0	\$2,000

Progress Reports

Critical Tasks

Task ID	Task Name	Planned Finish Date	Actual Finish Date	Status	
1	Project Initiation	2024-07-16	2024-07-16	Completed	
2	Requirement Gathering	2024-07-21	2024-07-22	Completed	
3	Site Structure Planning	2024-07-24	2024-07-25	Completed	
4	Design Phase	2024-08-03	2024-08-05	Completed	
5	Design Review and Approval	2024-08-07	2024-08-09	Completed	
6	Development Phase	2024-08-27	In Progress	On Schedule	
8	Integration and Testing	2024-09-13	-	Not Started	
9	User Acceptance Testing (UAT)	2024-09-18	-	Not Started	
10	Final Revisions	2024-09-22	-	Not Started	
11	Deployment	2024-09-25	-	Not Started	
12	Project Closure	2024-09-27	-	Not Started	

Milestone Report

Milestone	Planned Date	Actual Date	Status
Project Kickoff	2024-07-15	2024-07-15	Completed
Requirement Document	2024-07-21	2024-07-22	Completed

Milestone	Planned Date	Actual Date	Status
Site Map Created	2024-07-24	2024-07-25	Completed
Initial Design Completed	2024-08-03	2024-08-05	Completed
Design Approved	2024-08-07	2024-08-09	Completed
Frontend and Backend Completed	2024-08-27	-	In Progress
Content Ready	2024-09-06	-	In Progress
Testing Completed	2024-09-13	-	Not Started
UAT Completed	2024-09-18	-	Not Started
Revisions Completed	2024-09-22	-	Not Started
Site Live	2024-09-25	-	Not Started
Project Completed	2024-09-27	-	Not Started

Slipping Tasks

Task ID	Task Name	Planned Finish Date	Actual Finish Date	Status	Delay
2	Requirement Gathering	2024-07-21	2024-07-22	Completed	1 Day
3	Site Structure Planning	2024-07-24	2024-07-25	Completed	1 Day
4	Design Phase	2024-08-03	2024-08-05	Completed	2 Days
5	Design Review and Approval	2024-08-07	2024-08-09	Completed	2 Days

This table captures the detailed status and monitoring elements of the Website Design project, including dashboards for project overview, cost overview, and upcoming tasks, as well as various resource, cost, and progress reports.
